

8.0 MONTHLY PROGRESS REPORT:

SHOWHOUSE: TARGET 99% COMPLETION	TARGET	ACHIEVED	COMMENT
Scheming + undercoat	May-23	100%	Completed
Cabinetry	May-23	100%	Completed
Electrical and Plumbing Fixtrues	May-23	100%	Completed
Tiling	Jun-23	100%	Completed
Furnishing of showhouse	Jun-23	20%	In progress

9.0 MONTHLY PROGRESS REPORT:


ELECTRICAL & PLUMBING PIPING	TARGET	ACHIEVED	COMMENT
Groundfloor, 1st and 2nd Floor	May-23	100%	Completed
3rd and 4th Floor	June - 23	100%	Completed

12.0 MONTHLY PROGRESS REPORT:

IRON MONGERY & DOOR FRAMES	TARGET	ACHIEVED	COMMENT
Groundfloor	May-23	100%	Completed
1st floor	June - 23	100%	Completed
2nd floor	July - 23	20%	In progress
3rd Floor	Aug-23	0%	Scheduled
4th Floor	Sep-23	0%	Scheduled

13.0 MONTHLY PROGRESS REPORT:

HOUSES + CORRIDOR PLASTER	TARGET	ACHIEVED	COMMENT
Groundfloor	Jun-23	100%	Ahead of Scheduled
1st floor	July - 23	80%	In progress
2nd floor	Aug - 23	0%	Scheduled
3rd Floor	Sept-23	0%	Scheduled
4th Floor	Oct-23	0%	Scheduled

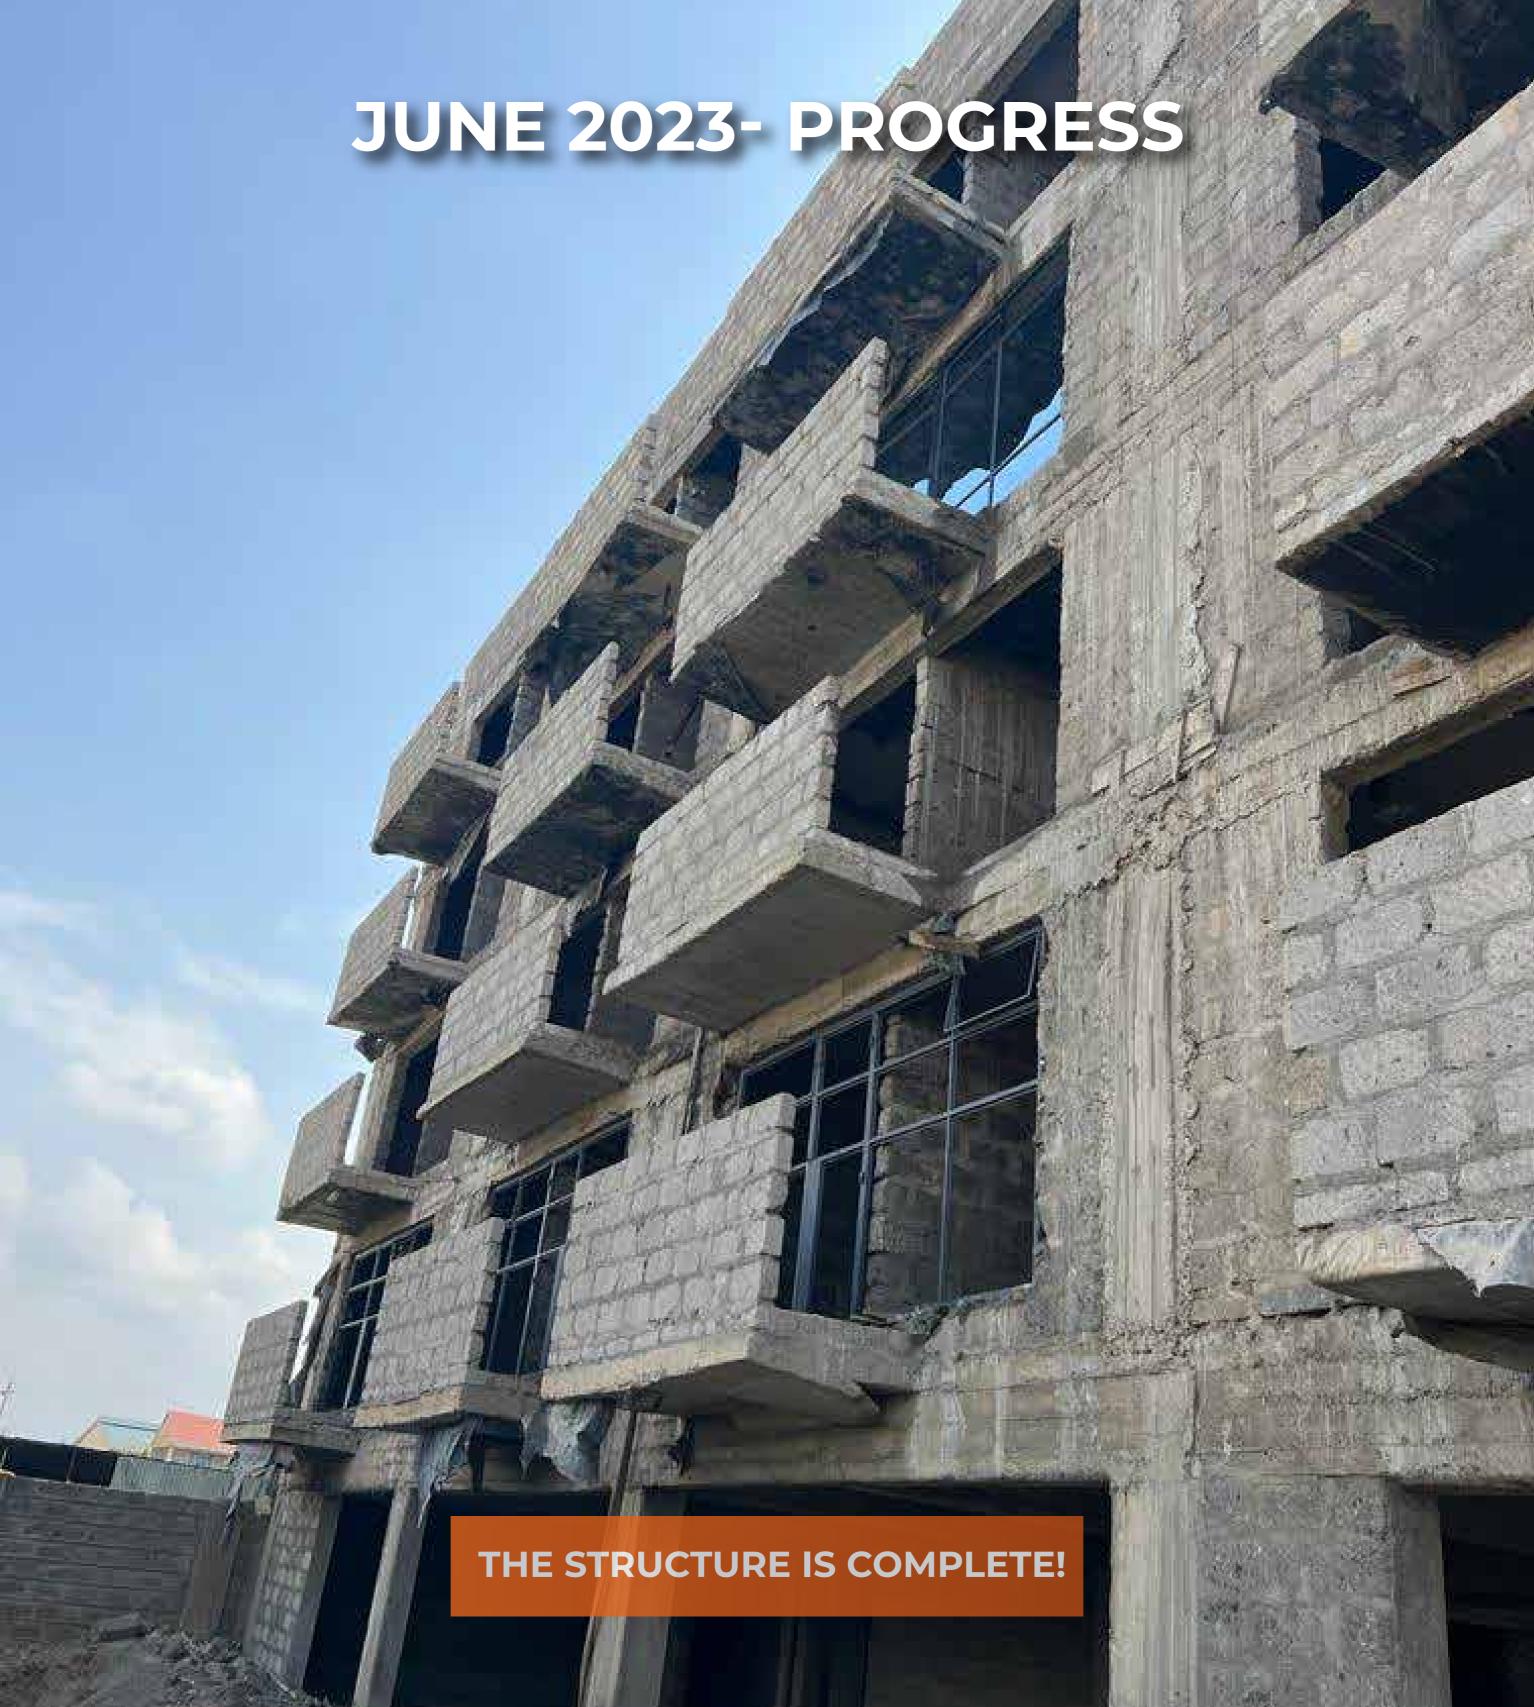





SHOW HOUSE IS COMPLETE



Browncap now has a customer portal that allows customers to access their customer statements digitally. The customer log in credentials will be sent on 10^{TH} July.





LOCATION

OPP. KENYATTA UNIVERSITY REFERRAL HOSPITAL EASTERN BYPASS, NAIROBI

CONTACTS

- 011 520 5332
- ✓ sales@imelaplace.co.ke
- www.127imelaplace.co.ke
